




1142 River Road
 New Castle, DE 19720
 855-738-7200

Certified Installation Data Sheet

Job Site Address:		Project Description:	
Residence		Ground Mount Solar Support Structure Installation	
Street		Company	
City		Permit #:	
Installer:		Installation Date:	

Sketch of Worksite

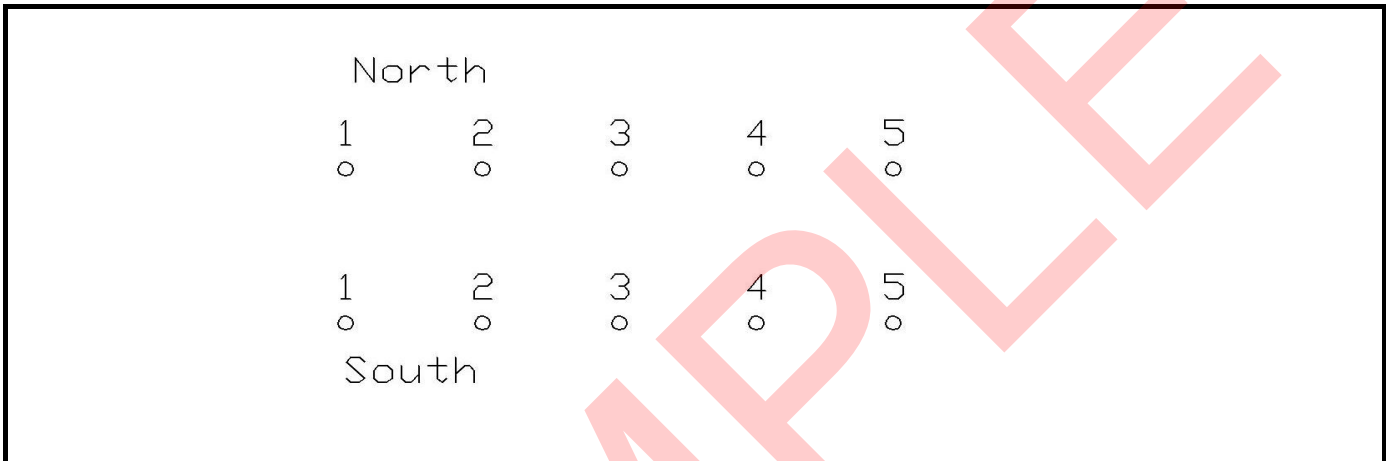

Pile Installation Field Data

Planetary: L5K Motor: X WR130 WR160 WR200 Back Pressure: 250 psi

North Post #	Post Type	Head Pressure	Axial Capacity	Depth*	Above Grade	South Post #	Post Type	Head Pressure	Axial Capacity	Depth*	Above Grade
1	CF-7	1,500	9,960	69"	18	1	CF-10	1,000	5,740	78"	48
2	CF-7	1,200	7,436	69"	18	2	CF-10	1,000	5,740	78"	48
3	CF-7	1,800	12,583	69"	18	3	CF-10	1,000	5,740	78"	48
4	CF-7	1,000	5,740	69"	18	4	CF-10	1,100	6,588	78"	48
5	CF-7	1,000	5,740	69"	18	5	CF-10	1,100	6,588	78"	48

The Solar Foundations USA system installed at the above location was installed, inspected and reported as per all manufacturer's specifications and requirements. All work was performed by technicians trained and certified by the manufacturer. This Installation Data Sheet contains all relevant information required by the manufacturer.

Certified Installer Signature:	Engineer (If Applicable):
---------------------------------------	----------------------------------

* Depth indicated is as installed in reference to existing grade at time of installation.
